



Measurements recorded in: Metric Imperial

Tag#: A349808

Page ___ of ___

Well Owner's Information

First Name: GURR, Last Name/Organization: BUILDING SERVICES, Mailing Address: [Redacted], E-mail Address: [Redacted]

Address of Well Location: [Redacted], Township: BEDFORD, City/Town/Village: SOUTH FRONTENAC, Lot: 1a, Concession: 11, County/District/Municipality: FRONTENAC, Province: Ontario, Postal Code: [Redacted], UTM Coordinates: NAD 83 18 384133 19401174, Municipal Plan and Sublot Number: NORTH LOT

Overburden and Bedrock Materials/Abandonment Sealing Record table with columns: General Colour, Most Common Material, Other Materials, General Description, Depth (m/ft) From, To. Rows include BROWN SAND, GREY/RED GRANITE, GREY GRANITE, RED GRANITE.

Annular Space table with columns: Depth Set at (m/ft) From, To; Type of Sealant Used (Material and Type); Volume Placed (m³/ft³). Row: 20 0 CEMENT 7 FT 3

Results of Well Yield Testing table with columns: After test of well yield, water was; Draw Down (Time, Water Level); Recovery (Time, Water Level). Includes notes like 'CUSTOMER GETTING WELL' and 'FRACTURED'.


Method of Construction and Well Use checkboxes. Method of Construction: Air percussion checked. Well Use: Domestic checked.

Construction Record - Casing table with columns: Inside Diameter, Open Hole OR Material, Wall Thickness, Depth (m/ft) From, To; Status of Well checkboxes. Rows: 6 1/4" STEEL, 6" OPEN HOLE.

Construction Record - Screen table with columns: Outside Diameter, Material, Slot No., Depth (m/ft) From, To; Status of Well checkboxes.

Water Details and Hole Diameter tables. Water Details: Depth, Kind of Water. Hole Diameter: Depth, Diameter.

Well Contractor and Well Technician Information form. Business Name: BACK KNOX WELL DRILLING LTD, Address: 580 PERTH RD, Municipality: GLENBURNE.

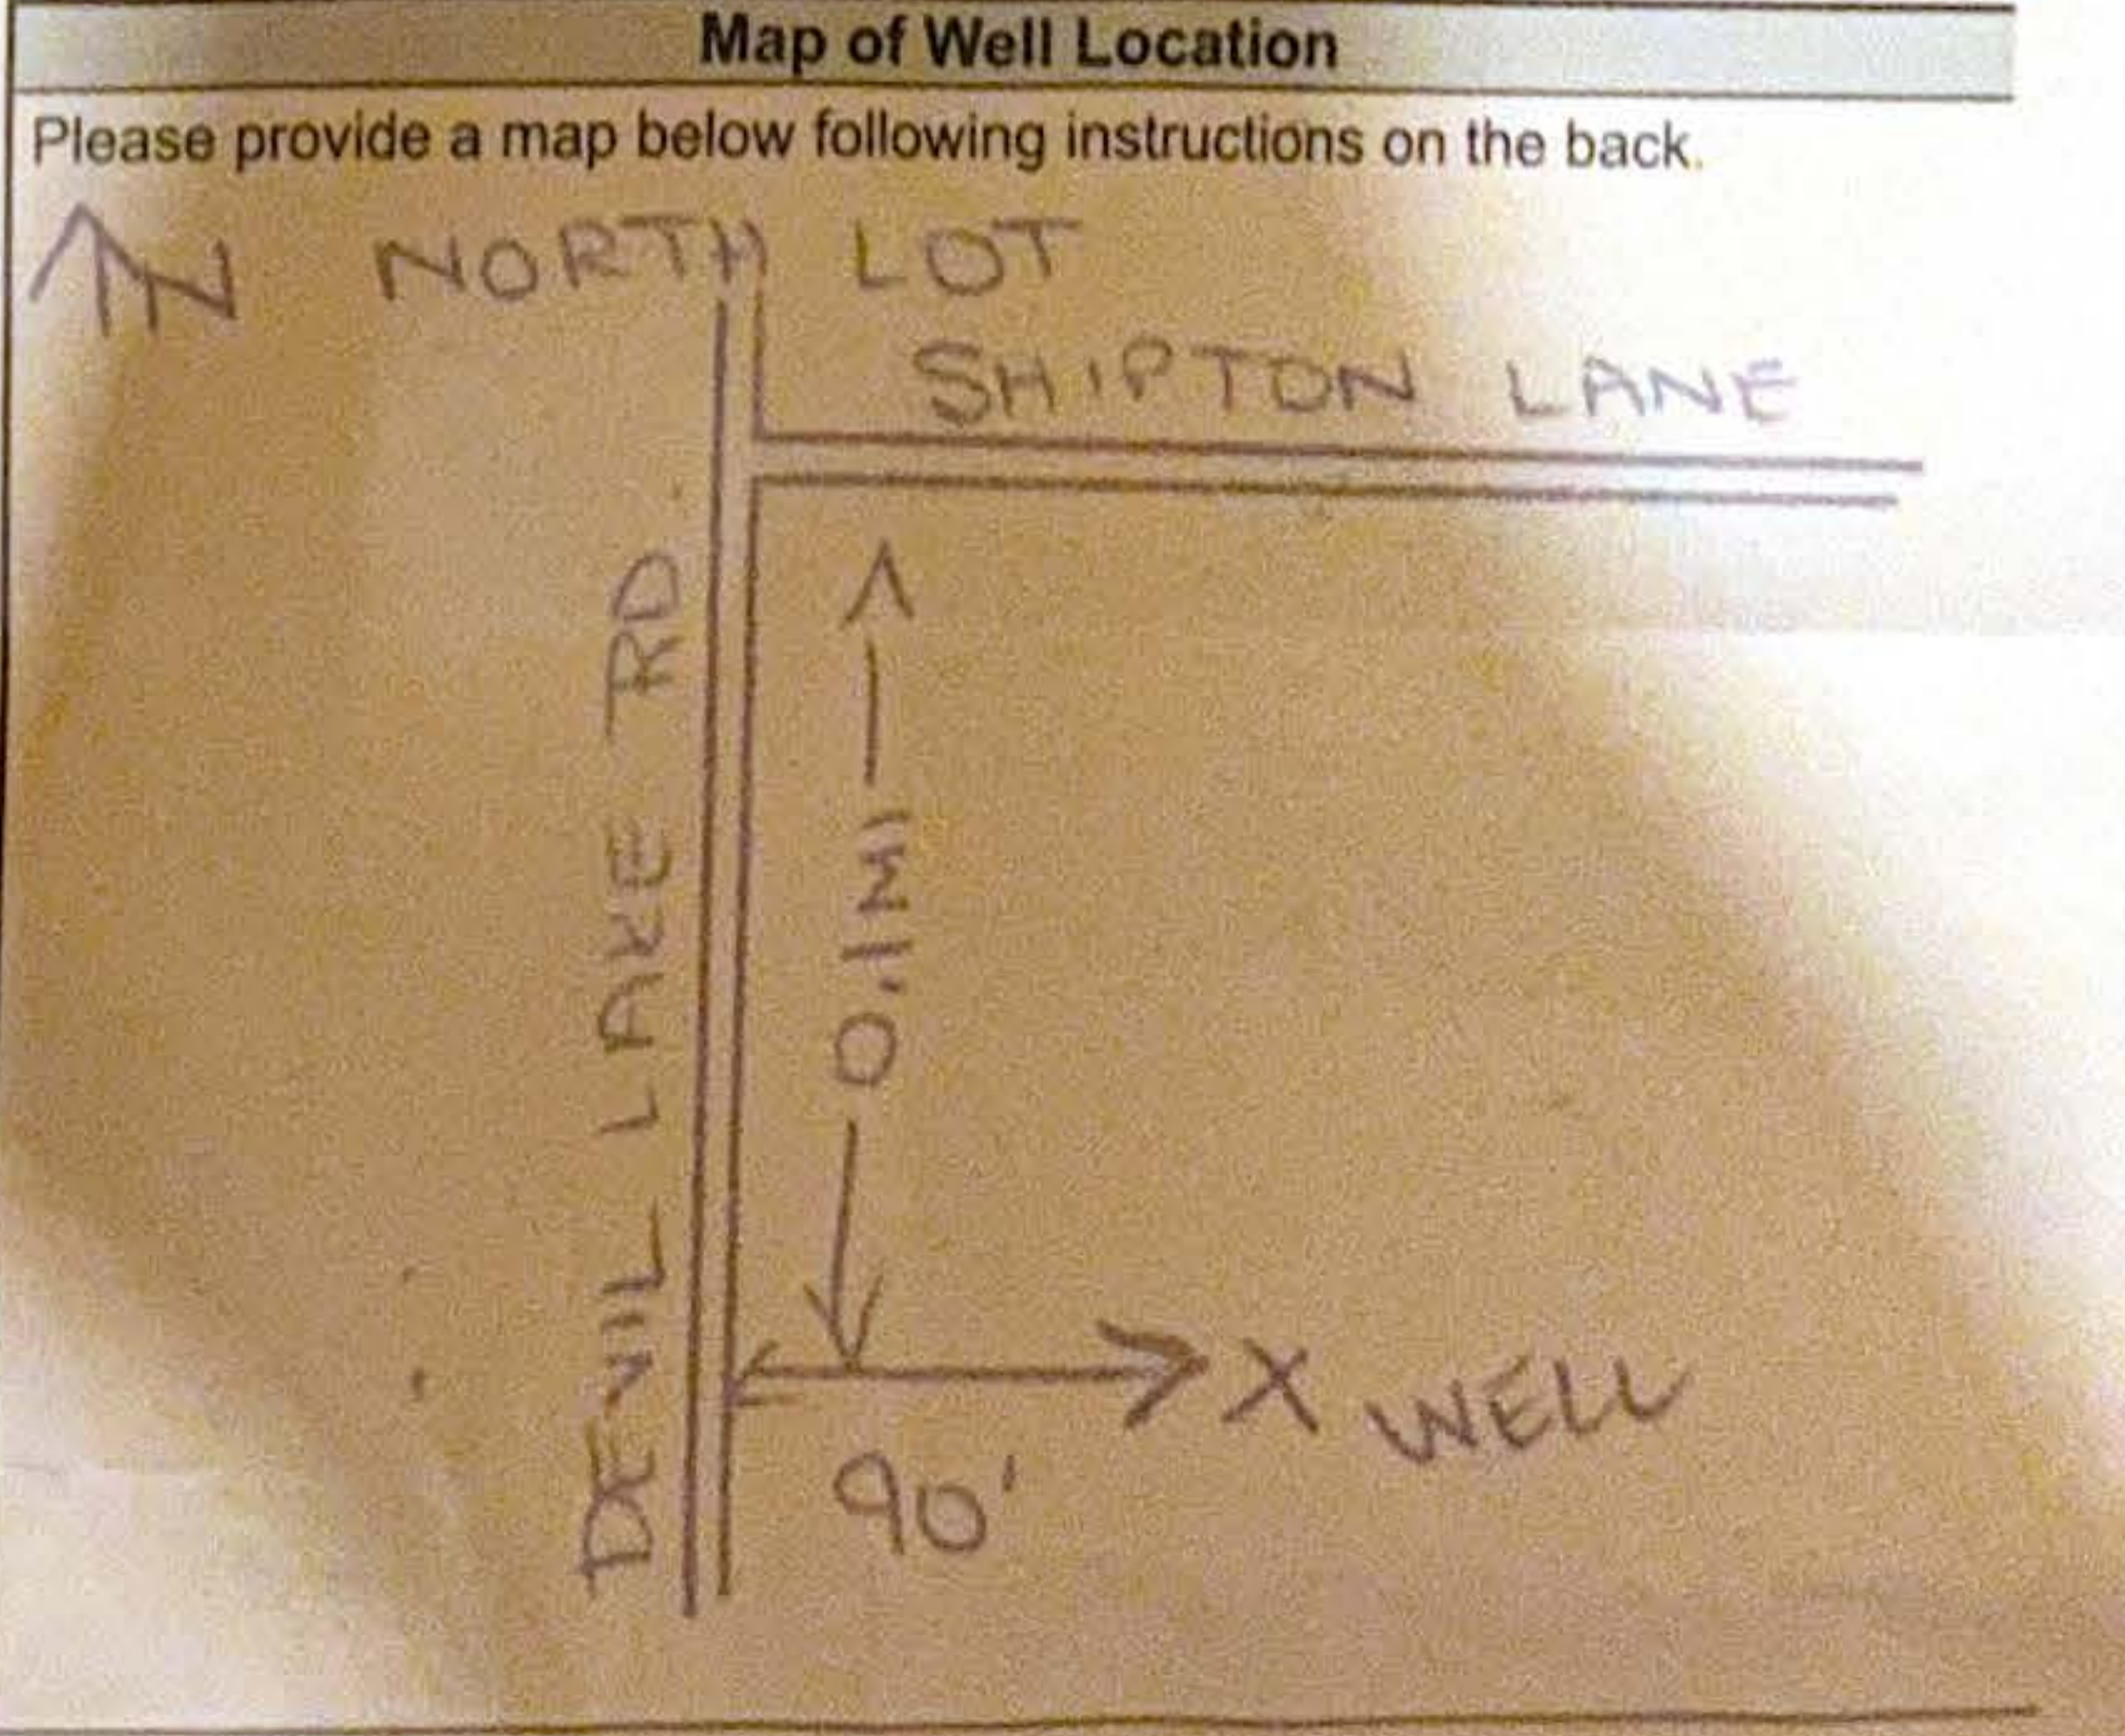

Well Contractor and Well Technician Information form. Business Name: BACK KNOX WELL DRILLING LTD, Address: 580 PERTH RD, Municipality: GLENBURNE.

Ministry Use Only section. Audit No: 394471, Date Package Delivered: 2022 MAR, Date Work Completed: [Blank].



JACK KNOX WELL DRILLING LTD.

BOX 33
 GLENBURNIE, ONTARIO
 K0H 1S0

WELL PUMP TEST ---6 HOUR

Date SEPT 13/22

NAME GURR BUILDING SERVICES

ADDRESS [REDACTED]

TOWNSHIP SOUTH FRONT LOT 12 CON 11 BLDG LOT _____ PLAN _____
BEDFORD

NORTH LOT

PUMPING	RECOVERY
_____	1MIN _____
_____	2MIN _____
_____	3MIN _____
_____	4MIN _____
<u>20</u>	5MIN _____
_____	6MIN _____
_____	7MIN _____
_____	8MIN _____
_____	9MIN _____
<u>29.7</u>	10MIN _____
<u>38</u>	15MIN _____
<u>45</u>	20MIN _____
<u>52</u>	25MIN _____
<u>59</u>	30MIN _____
<u>78.2</u>	45MIN _____
<u>95.3</u>	60MIN _____
<u>147.3</u>	2HRS _____
<u>177.1</u>	3HRS _____
<u>199.4</u>	4HRS _____
<u>217.1</u>	5HRS _____
<u>233.1</u>	6HRS _____

STATIC LEVEL 10.7' PUMP RATE 3 1/2 G.P.M

WATER LEVEL END OF PUMPING 233.1'

REMARKS: WELL TAG #A349808

WELL IS 325' DEEP

RECOMMENDED PUMP DEPTH 320'
RECOMMENDED RATE 4 G.P.M.

Ron Knox

Ron Knox
