

SEWAGE SYSTEM CERTIFICATE OF APPROVAL

The Approval number for the sewage disposal system at this building is:

BE - 27 - 17
district - number - year

&A
Health

Please refer to this number when requesting any information from the KFL&A Public Health.

The sticky label enclosed with your Final Inspection Report is to be affixed to your home's electrical panel or fuse box.

The number of the label should be used when requesting information about your septic system from your area Public Health office. It will also be valuable in the event your house is sold, as it will make searching for documents easier.

Please help by affixing your sticker to your panel.

Thank you.

Environmental Health Department
KFLA Public Health

**KINGSTON, FRONTENAC AND LENNOX & ADDINGTON PUBLIC HEALTH
FINAL INSPECTION REPORT FOR CLASS 2, 3, 4, 5 SEWAGE SYSTEM**


Inspection Details

OWNER [REDACTED] INSTALLER **J.T. Martin Excavating Ltd.
Justin Martin**

1. Work has been satisfactorily completed and includes:

- a) Septic tank / holding tank / treatment unit of working capacity of 4141 litres constructed of concrete plastic serving 3
- Make / Model of Tank: 1060 Infiltrator
- b) Leaching / Filter Bed 24.3 metres of 4" / 100 mm diameter distribution pipe of Royal (type and product description) laid in 4 runs and fed by Gravity. If Filter Bed: Loading Area 32.5 m² Contact Area _____ m²
- c) Treatment Unit Make / Model: _____ Level _____
- d) Chamber System Make / Model: _____ # of Pieces: _____
- e) Leaching Bed GPS Coordinates: Latitude N 44°35'11.9" Longitude W 076°28'53.9"

2. Location: The sketch below indicates the location of all components of the Sewage System and separation distances as required under the Ontario Building Code.

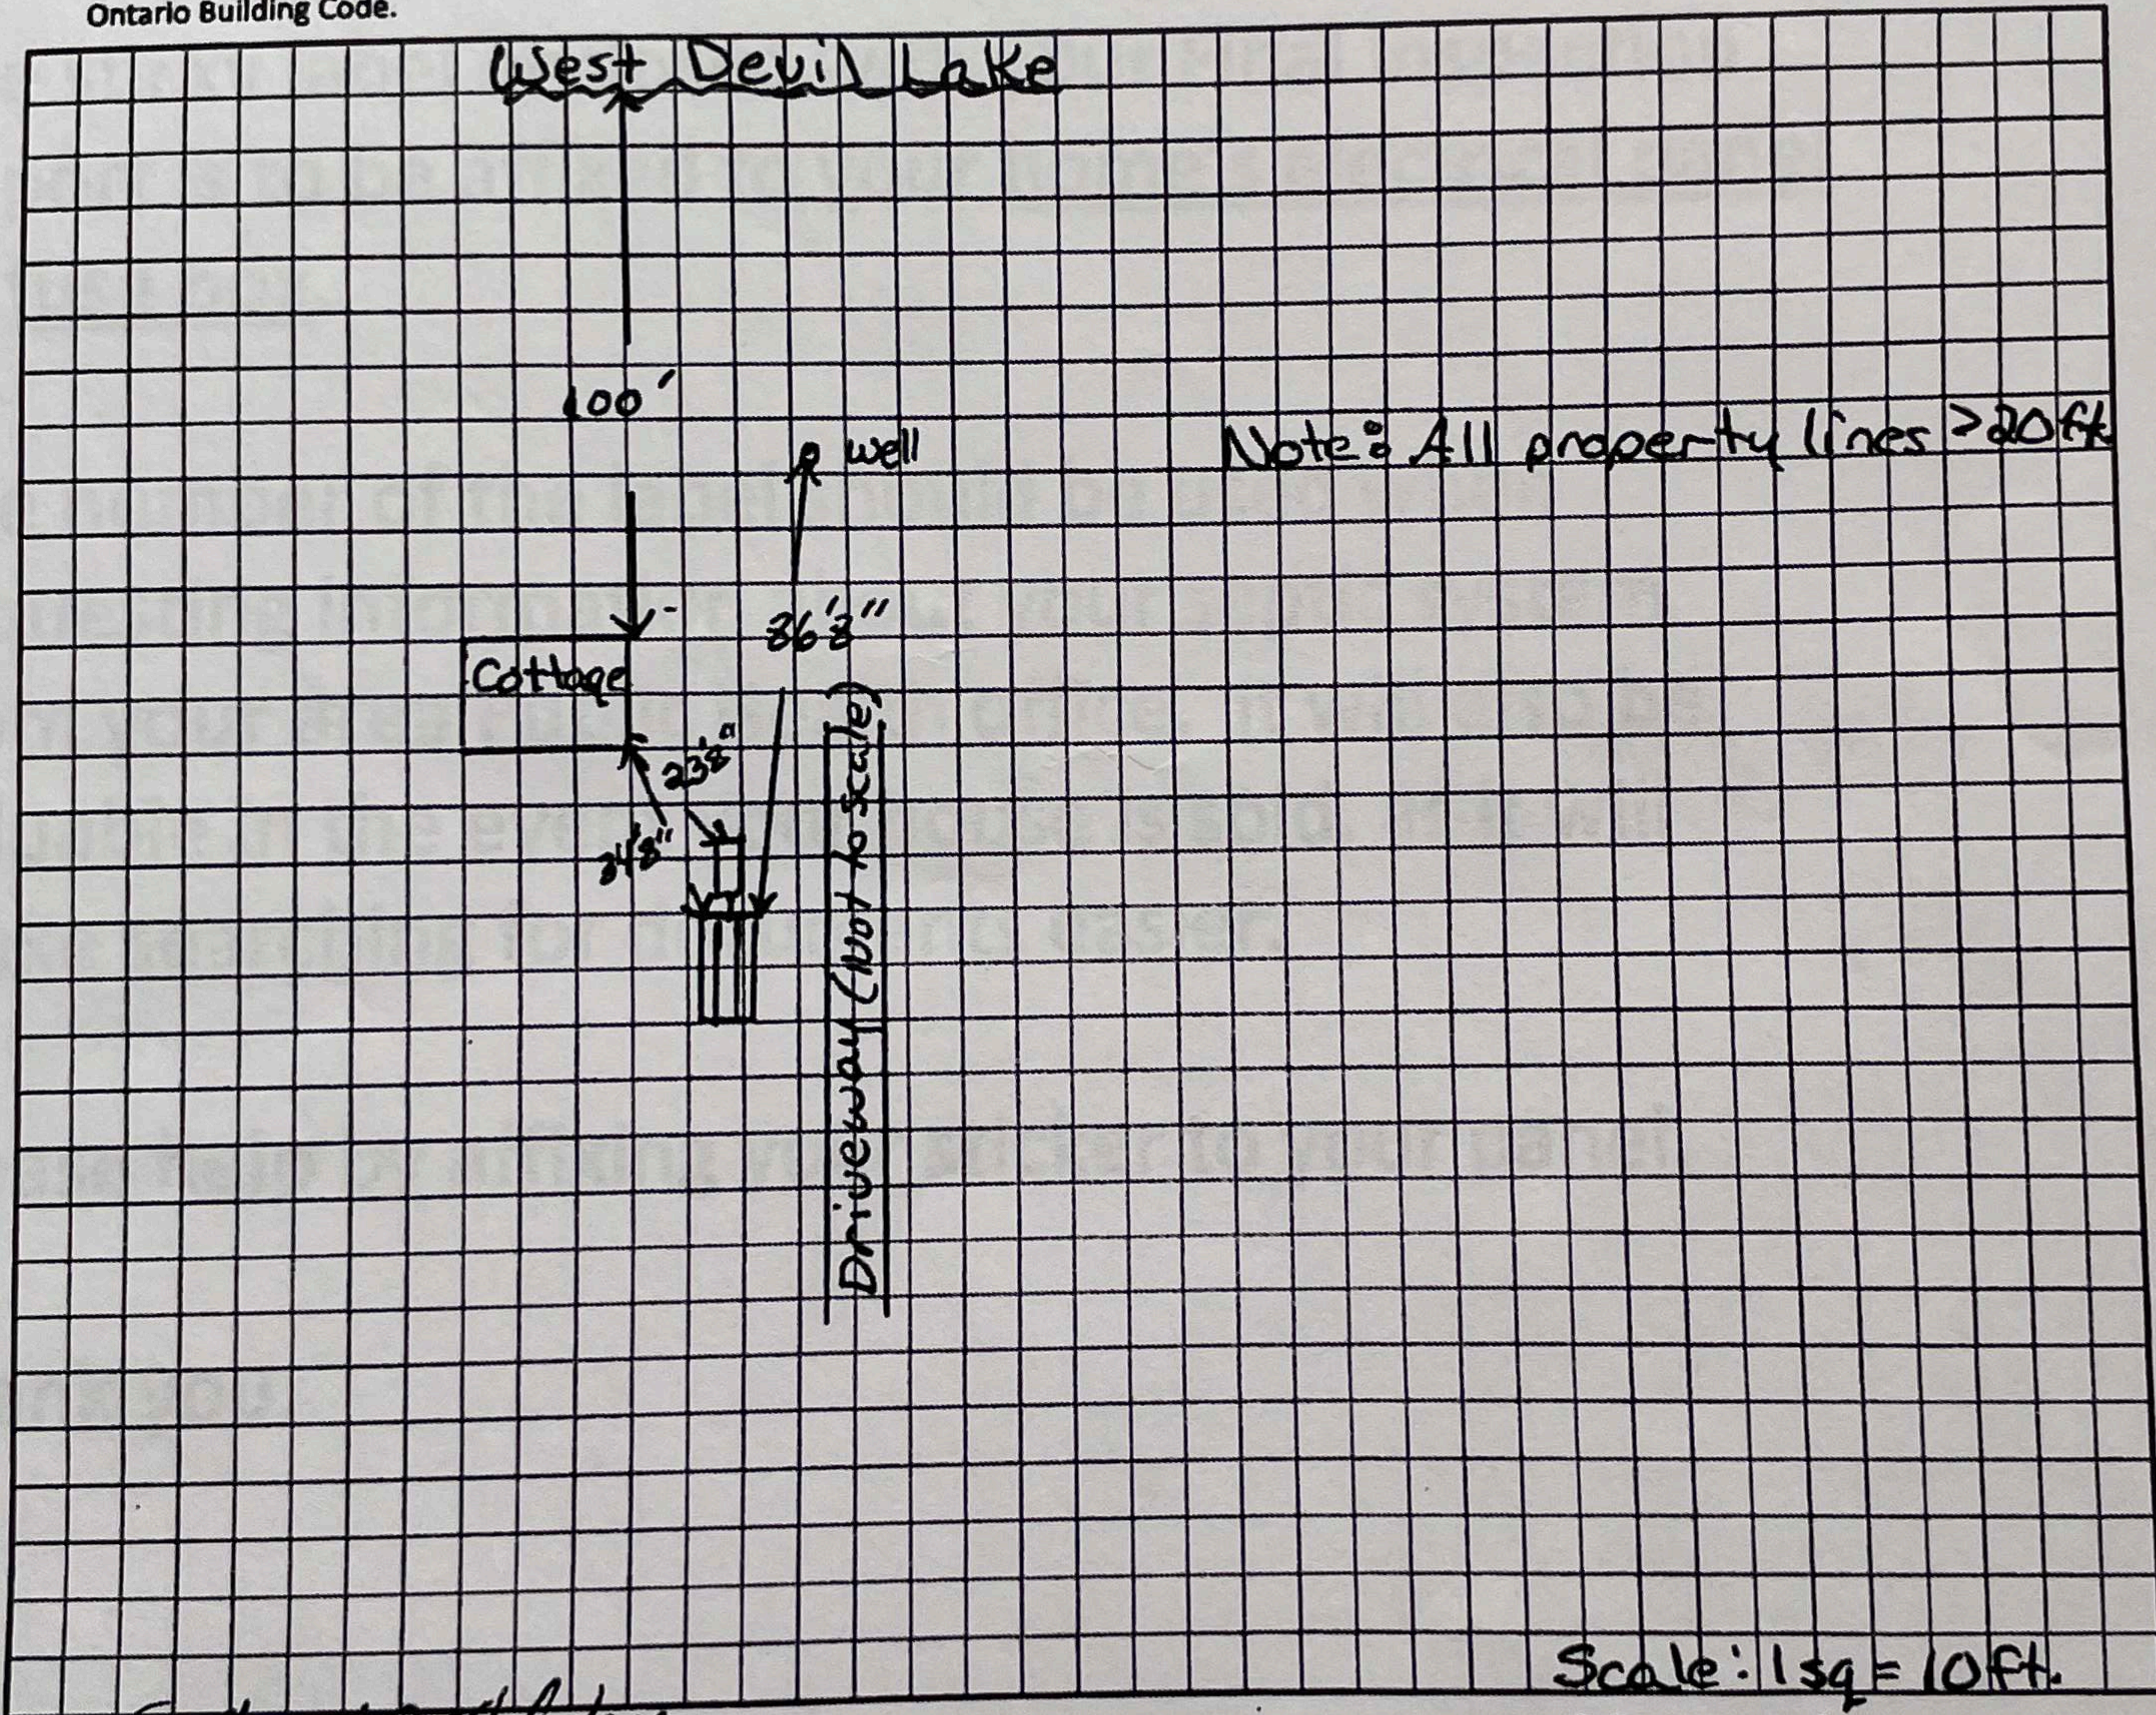

Inspector [Signature] Inspection Date May 14, 2018

The Sewage System was inspected and it has been determined that the installation complies with the requirements of Regulation 332/12 made under the Building Code Act for the following property located on Lot 9 Concession 10 Municipality S. Frontenac
District Bedford Municipal address 199 West Devil Lake Lane
Registered Plan # 13R-20434 Part(s) _____ Plan of Subdivision # _____ Sublot _____

Final Compliance Inspection – the following work has been completed:

- System has been backfilled with suitable granular fill Grading to shed run-off and divert water around leaching bed has been completed
- Sloped surfaces are stabilized Topsoil has been put on the leaching bed to establish grass cover
- Other: _____

Inspector [Signature] Date July 5, 2018

2730258 ONTARIO LTD.
Operating As BRYAN'S SEPTIC SERVICE

HST #75775070

Bryan Colford

Septic Tank Pumping & Liquid Waste Dis


P.O. Box 37, Westport, Ontario K0G 1X

(613) 273-3078 Mobile (613) 264-3

e-Transfer payment with invoice # to

btcolford@hotmail.com

CUSTOMER



DATE

11/04-23

NAME

ADDRESS

199 West Dew/lat

CASH

CHARGE

CHEQUE

DEBIT
CARD

C.O.D.

ON ACCT.

PAID OUT

*Pumped 1000 gal
 Septic Tank
 Cleaned filter
 Chg
 By*

SPECIAL INSTRUCTIONS

*Everything in
 good condition*

SUBTOTAL

HST / GST

579.00

e. Transfer

Net 30 days. 2% per month on overdue accounts.

All claims and returned goods MUST be accompanied by this bill.

PST

SOLD BY

RECEIVED BY

TOTAL

539.00

41274

Product 609

THANK YOU
