Ministry of the Environment
Ontario

The Ontario Water Resources Act

WATER WELL RECORD

1. PRINT ONLY IN SPACES PROVIDED
2. CHECK ☒ CORRECT BOX WHERE APPLICABLE

11 | 2213479 | MUNICIP 22002 | CON. CON 05

COUNTY OR DISTRICT	TOWNSHIP, BOROUGH, CITY, TOWN, VILLAGE	CON. BLOCK, TRACT, SURVEY, ETC	LOT 25-27
Frontenac	Bedford	5	25&26

[redacted] 3 North Gore, Ontario K0A 2T0

DATE COMPLETED 48-53: DAY 10 MO Dec YR 90

RING | RC | ELEVATION | RC | BASIN CODE | II | III | IV

LOG OF OVERBURDEN AND BEDROCK MATERIALS (SEE INSTRUCTIONS)

GENERAL COLOUR	MOST COMMON MATERIAL	OTHER MATERIALS	GENERAL DESCRIPTION	DEPTH - FEET FROM	TO
brown	soil			0	1
white	limestone			1	120

31

32

41 WATER RECORD

WATER FOUND AT - FEET	KIND OF WATER
70'	1 ☐ FRESH 2 ☐ SALTY 3 ☐ SULPHUR 4 ☐ MINERALS 5 ☐ GAS — UNTESTED
118'	1 ☐ FRESH 2 ☐ SALTY 3 ☐ SULPHUR 4 ☐ MINERALS 5 ☐ GAS — UNTESTED
	1 ☐ FRESH 2 ☐ SALTY 3 ☐ SULPHUR 4 ☐ MINERALS 6 ☐ GAS
	1 ☐ FRESH 2 ☐ SALTY 3 ☐ SULPHUR 4 ☐ MINERALS 6 ☐ GAS
	1 ☐ FRESH 2 ☐ SALTY 3 ☐ SULPHUR 4 ☐ MINERALS 6 ☐ GAS

51 CASING & OPEN HOLE RECORD

INSIDE DIAM INCHES	MATERIAL	WALL THICKNESS INCHES	DEPTH - FEET FROM	TO
6 1/4	1 ☐ STEEL 2 ☐ GALVANIZED 3 ☐ CONCRETE 4 ☐ OPEN HOLE 5 ☐ PLASTIC	.188	0	22
	1 ☐ STEEL 2 ☐ GALVANIZED 3 ☐ CONCRETE 4 ☐ OPEN HOLE 5 ☐ PLASTIC			
	1 ☐ STEEL 2 ☐ GALVANIZED 3 ☐ CONCRETE 4 ☐ OPEN HOLE 5 ☐ PLASTIC			

SCREEN

SIZE(S) OF OPENING (SLOT NO.)	DIAMETER INCHES	LENGTH FEET
MATERIAL AND TYPE	DEPTH TO TOP OF SCREEN FEET	

61 PLUGGING & SEALING RECORD

DEPTH SET AT - FEET FROM	TO	MATERIAL AND TYPE (CEMENT GROUT, LEAD PACKER, ETC.)
0	20	grout

71 PUMPING TEST

PUMPING TEST METHOD: 1 ☑ PUMP 2 ☐ BAILER

PUMPING RATE: 6 GPM

DURATION OF PUMPING: 1 HOURS ___ MINS

STATIC LEVEL	WATER LEVEL END OF PUMPING	WATER LEVELS DURING (1 ☐ PUMPING 2 ☐ RECOVERY) 15 MINUTES	30 MINUTES	45 MINUTES	60 MINUTES
31 FEET	120 FEET	120 FEET	120 FEET	120 FEET	120 FEET

IF FLOWING, GIVE RATE: ___ GPM

PUMP INTAKE SET AT: ___ FEET

WATER AT END OF TEST: 1 ☑ CLEAR 2 ☐ CLOUDY

RECOMMENDED PUMP TYPE: ☐ SHALLOW ☑ DEEP

RECOMMENDED PUMP SETTING: 115 FEET

RECOMMENDED PUMPING RATE: 6 GPM

LOCATION OF WELL

IN DIAGRAM BELOW SHOW DISTANCES OF WELL FROM ROAD AND LOT LINE. INDICATE NORTH BY ARROW.

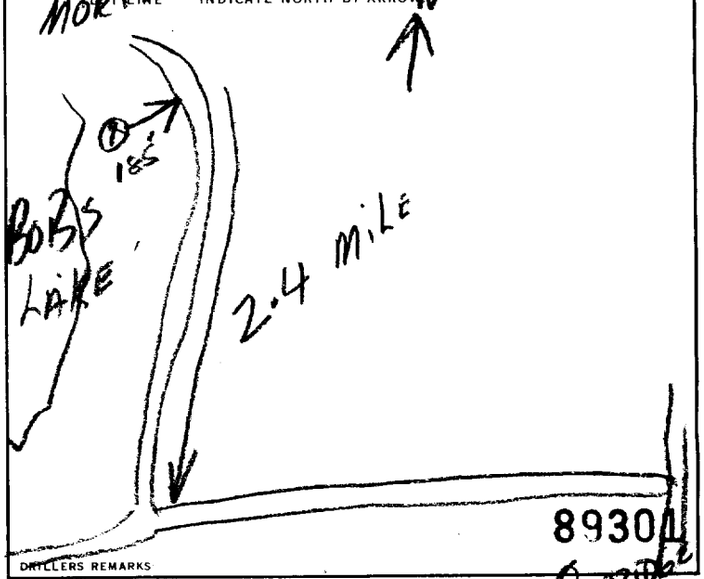

DRILLERS REMARKS: 89304

FINAL STATUS OF WELL	1 ☑ WATER SUPPLY 2 ☐ OBSERVATION WELL 3 ☐ TEST HOLE 4 ☐ RECHARGE WELL 5 ☐ ABANDONED, INSUFFICIENT SUPPLY 6 ☐ ABANDONED, POOR QUALITY 7 ☐ UNFINISHED ☐ DEWATERING
WATER USE	1 ☑ DOMESTIC 2 ☐ STOCK 3 ☐ IRRIGATION 4 ☐ INDUSTRIAL ☐ OTHER 5 ☐ COMMERCIAL 6 ☐ MUNICIPAL 7 ☐ PUBLIC SUPPLY 8 ☐ COOLING OR AIR CONDITIONING 9 ☐ NOT USED
METHOD OF CONSTRUCTION	1 ☐ CABLE TOOL 2 ☐ ROTARY (CONVENTIONAL) 3 ☐ ROTARY (REVERSE) 4 ☐ ROTARY (AIR) 5 ☑ AIR PERCUSSION 6 ☐ BORING 7 ☐ DIAMOND 8 ☐ JETTING 9 ☐ DRIVING ☐ DIGGING ☐ OTHER

CONTRACTOR

NAME OF WELL CONTRACTOR: DALY WELL DRILLING LIMITED

WELL CONTRACTOR'S LICENCE NUMBER: 1704

ADDRESS: Verona, Ontario K0H 2W0

NAME OF WELL TECHNICIAN: Mr. Albertson

WELL TECHNICIAN'S LICENCE NUMBER:

SIGNATURE OF TECHNICIAN/CONTRACTOR: per M Young

SUBMISSION DATE: DAY 10 MO Dec YR 90

OFFICE USE ONLY

DATA SOURCE: 58

CONTRACTOR: 1704

DATE RECEIVED: APR 09 1991

DATE OF INSPECTION:

INSPECTOR:

REMARKS:

CSS.ES

MINISTRY OF THE ENVIRONMENT COPY

FORM NO. 0506 (11/86) FORM 9
